

DIRECTORATE: ENGINEERING SERVICES: MONTHLY REPORT - P.M.U DEPARTMENT AS AT END FEBRUARY 2022
(9/2/1/5) (MANAGER: PMU)

PURPOSE

To submit a report to the Director Engineering Services and Council regarding the current projects/works and or assignments undertaken by the Project Management Unit for the 2021/2022 financial year.

BACKGROUND

The PMU department is currently actively undertaking the following assignments for various departments within the Langeberg Municipality. See status report on all active projects / works and assignments performed by the Project Management Department for the month of February 2022 that included detailed specification and tender documentation for various operational and capital projects. This report also indicates the status quo on all MIG/MIS projects and applications accordingly.

MIG/MIS PROJECTS

Project Details	Project Cycle Status and Progress	Mid Term Status – (In-put)	Final Phase Status (Out-put)
MUNICIPAL INFRASTRUCTURE GRANT	<p><i>This department is tasked with the administration of the Municipal Infrastructure Grant this takes the form of the following ongoing monthly reporting in both hard copy format and on the MIG Municipal Information System (MIG MIS):</i></p> <p><i>Monthly Quarterly Reporting of all progress made on MIG projects.</i></p> <p><i>Submitting of the financial claims (MIG8) on MIG MIS.</i></p> <p><i>Submitting of MIG 4 claims</i></p> <p><i>Submitting of MIG 9 documentation on projects completed</i></p> <p><i>A MIG 1, including a Technical report and Beneficiary report, application has been submitted via the MIG MIS and email for the planned MIG project</i></p> <p>UPGRADING OF THE ROBERTSON WWTW</p>	<p>Contact made with MIG office pertaining to Robertson WWTW, additional info required. Have forwarded such request to the Director Engineering Services and await response.</p> <p>WEC consulting Engineers appointed and is currently within the appeals period.</p> <p>Monthly Quarterly reports submitted, MIG MIS captured</p> <p>Addressing the “backlog” completion of projects completed as per MIG MIS requirements</p> <p>MIG 1 and supporting documents submitted DLG MIG and MISA and we expect to have the project appraised in early 2022</p> <p>MISA has supported the technical report for Robertson WWTW and an appraisal meeting is expected in February 2022</p>	

CAPITAL PROJECTS

Project Details	Project Cycle Status and Progress	Mid Term Status – (In-put)	Final Phase Status (Out-put)
<p>❖ T40/2020 UPGRADING AND REHABILITATION OF THE WATER NETWORKS IN ASHTON ZOLANI - LANGE BERG MUNICIPALITY.</p>	<p><i>The project management unit is currently compiling detailed plans and documentation for the before mentioned planned project. Plans are to include all required details, existing services etcetera. Detailed tender document is currently being drafted and it is estimated that the tender will be advertised in Mid / late October 2020. The estimated value of this tender amounts to R4 600 000.00 and is being undertaken on behalf of the Department Civil Engineering Services.</i></p> <p><i>Detailed tender drawings completed on 28 October 2020. Tender document has been completed and will be forwarded to the BSC on 02 November 2020 for approval. It is anticipated that the tender will be advertised in Mid-November to close Mid December. Tender advertised 13 November 2020, compulsory clarifications meeting held on 27 November 2020. Tender closes on 18 December 2020. It is envisaged that project commencement will take place in early March 2021.</i></p> <p><i>Tender report completed and submitted to BEC on 27 January 2021, await the outcome of the BAC Awarded. Appeals period ends 02 March 2021.</i></p>	<p>Contracted has commenced with works.</p> <p>Practical completion achieved on all works other than the Breede River Bridge crossing in Bonnievale which is set to be completed in early December 2021.</p> <p>Project completion achieved on 15 December 2021.</p>	<p>Project will be completed within 2021/2022 book year.</p> <p>Project completed on 15 December 2021 and is now in 12 month defects liability period.</p>

Project Details	Project Cycle Status and Progress	Mid Term Status – (In-put)	Final Phase Status (Out-put)
❖ ASLA WSIG – Bulk Services	Site meeting held with Implementing Agent – Boekenhoutskloof and Mandela Square Montagu Bulk Service	Mandela Square has been handed over to the Contractor and we still await the outcome of the 24G application for Boekenhoutskloof. Construction at Mandala Square will commenced in January 2022 and works are expected to be completed in March 2022. 24G needs finalisation for Boekenhoutskloof with possible fine being paid	
❖ ASLA – Housing Top Structures ERF 136, Robertson	Construction of 172 new houses as per detailed designs	60 foundations complete 60 floors complete 58 tops/walls complete 27 roofs complete	Pictures attached.
❖ Q34/2021 – Architectural Services – Cogmanskloof Sportsgrounds – New Ablusion	Clarification meeting held 20 August 2021. Quotation closed on 27 August 2021. Report submitted to BEC on 15 September 2021. Await BAC outcome. Plans and supporting documents have been submitted to the Building Control Office for council approval.	Plans submitted for approval and approval has been received.	
❖ Q37/2021 – Professional Architecture Services – Robertson Traffic Offices	Advertised. Clarification meeting held 20 August 2021. Quotation closed on 27 August 2021. Report submitted to BEC on 15 September 2021. Await BAC outcome.	Awarded on 08 October 2021 – Architectural Services Kick off meeting held and sketch plans have been received. Plans and supporting documents have been submitted to the Building Control Office for council approval. Await the final outcome and plan approval Plans approved and construction tender advertised 11 February 2022.	
❖ T27/2021 – Provision of Architectural Services – New Fire Station Precinct - Robertson	Tender report submitted to BAC, await outcome and appeals period.	Tender awarded to TUSK CONSTRUCTION SUPPORT SERVICES (PTY) LTD.	

		<p>Detailed designs are being undertaken and should be completed towards the end of October 2021 Await the final designs and council approval</p> <p>Plans and supporting documents have been submitted to the Building Control Office.</p> <p>Approved plans received. It is anticipated that the construction tender will be advertised in August 2022.</p>	
<p>❖ T39/2021 – Development of Ashton Silo’s Cemetery expansion</p>	<p>Advertised 13th August 2021. Close 03 September 2021. Clarification meeting held 23 August 2021. Tender closed on 03 September 2021. Report submitted to BEC on 28 September 2021. Await BAC outcome</p>	<p>Awarded on 15 October 2021 (21 Day appeals period) – Professional Services Kick off meeting to be confirmed with professional service provider</p> <p>Service provider has submitted a detail programme of planned works.</p> <p>A meeting with the service provider is to take place in early February 2022.</p> <p>Meeting held on 09 February 2022 with all role players, the professional service provider to submit draft plans by 1st week of March 2022.</p>	
<p>❖ T44/2021 – Provision of Professional Engineering Services – New Material Recovery Facility, Ashton</p>	<p>Advertised. Closed 10 September 2021. Await BAC outcome. Professional Services Kick off meeting held on 30 November 2021.</p>	<p>Kick-off meeting held with service provider and programme of planned works received. A detailed survey of the site has been undertaken.</p> <p>Detailed designs underway, all designs are expected to be completed by end of February 2022</p> <p>Draft designs received and approved</p>	
<p>❖ T45/2021 – Supply and Install Fencing Material at various sites</p>	<p>Advertised. Tender closed on 23 September 2021. Await compliant documents and outcomes from the BEC.</p>	<p>Award made and currently in the appeals period, it is expected that works will commence in January 2022</p> <p>Await the official order from supply chain.</p> <p>Supplier Jetco has been on site and is awaiting materials to commence</p>	

		It has been confirmed that works will commence on 07 March 2022	
❖ T58/2021 Rehabilitation Of Filters At Montagu Water Treatment Works, Design And Construct	Advertised 15/10/2021. Tender closes on 05 November 2021 report submitted to BAC.	Tender has been awarded and will the project be managed further by the Civil Engineering department	
❖ Q29/2021 Air Conditioners	<i>Submitted to BSC, await outcome. Will be advertised in mid August 2021. Quotation closed on 20 August 2021. Report submitted to BEC on 14 September 2021. Await BAC outcome.</i>	Awarded on 19 October 2021 Contractor appointed and works to be completed by early January 2022. Works completed	Project completed January 2022.
❖ T29/2021 – Construction of 3.0ML Reservoir & Related Works (Robertson)	<i>Awarded – Objection period lapsed. Awarded for the design – Director Engineering Services is administering the contract. Construction tender to be advertised in November 2021 Tender closes 03 December 2021.</i>	Await BAC outcome Tender awarded and to be project managed by Director Engineering Services	
❖ T55/21 Professional Services: Design and Related Services – Bonnievale Telemetry System / Supervisory Control and Data Acquisition (Scada) System	<i>BSC held on 20th September 2021 Advertised on 23 September 2021 and closing on 15 October 2021. Technical evaluation report submitted to BEC on 26 October 2021 Service provider appointed and design underway.</i>	Awarded to IX consulting engineers and further project managed by Civil Engineering department	
❖ T56/21 Professional Engineering Services, Design and Implementation of Upgrades to Informal Trading Areas	<i>BSC held on 20th September 2021. Tender to be advertised 02 October 2021. Tender closed on 22 October 2021, await compliant documents from the BEC for the technical evaluation.</i>	UDS AFRICA appointed, kick off meeting held designs to be completed by end February 2022 Meeting with all role players was held on 08 February 2022. Designs will be received in 1 st week of March	
❖ T64/20201 Professional services Design and related services, Electrification of Housing project ERF 136	<i>Tender advertised and closed 19 November 2021 Await compliant documents from BEC</i>	Service provider appointed and currently in 21 day appeals period CMB Consulting Engineers appointed and kick off meeting held, designs to be completed by mid- February 2022.	

		Designs complete and document approved by BSC. Tender advertised on 25 February 2022	
❖ T30/2021 Design Supply and Install of High Mast	<i>Await tender documents from BEC for evaluation. Awarded on 27 September 2021 –hand over meeting held with the contractor. Contractor on site and excavations underway</i>	Construction underway and works are expected to be completed within the 2 nd quarter of 2022.	
❖ T52/2021 – Refurbishment of Roof structures – Community Facilities	<i>Advertised on 23 September 2021 Closing 22 October 2021. Tender closed on 22 October 2021, await compliant documents from the BEC for the technical evaluation. Tender awarded and currently in the appeals period</i>	Tender Awarded and Currently in The 21 Day Appeals Period. ZABS Enterprises appointed and kick off meeting held. Contractor commenced with works at Barnard Hall, Ashton Barnard hall and Ashton Town hall under construction. Two claims have been received and approved for payment	
❖ T54/2021 – Professional services – design and related services: Electrical Projects	<i>To be discussed at BSC on 04 October 2021. Advertised 23/10/2021. Tender advertised and closed on 12 November 2021. Await compliant documents from the BEC to evaluate.</i>	Await BAC outcome	
❖ Q02/2022 Pre-Fabricated Steel Catwalk, Bonnievale Water Works	<i>Advertised on 11 February 2022</i>	Clarifications meeting held on 18 February 2022. Tender closed on 25 February 2022. Only 1 tender received and offer above the R200 000.00 quotation threshold.	
❖ Q15/2022 Replace Malva Street No2 MS – Langeberg Municipality Electrical Department, Robertson	<i>Await BSC from Municipal Manager office</i>	Specifications and BOQ complete and will be submitted to the BSC for approval once BSC have been formulated.	
❖ Q16/2022 Replace Watsonia RMU Langeberg Municipality Electrical Department, Robertson	<i>Await BSC from Municipal Manager office</i>	Specifications and BOQ complete and will be submitted to the BSC for approval once BSC have been formulated.	
❖ Q17/2022 Replace Denne Avenue RMU Langeberg Municipality Electrical Department, Robertson	<i>Await BSC from Municipal Manager office</i>	Specifications and BOQ complete and will be submitted to the BSC for approval once BSC have been formulated.	

❖ Q18/2022 Install 95mm Electrical Cable – from Reits to White Street, Robertson - Langeberg Municipality Electrical Department, Robertson	<i>Await BSC from Municipal Manager office</i>	Specifications and BOQ complete and will be submitted to the BSC for approval once BSC have been formulated.	
❖ Q49/2021 Provision of occupational health and safety services (client agent), New Fire Station, Robertson			Quotation not awarded due to offers exceeding R200 000.00 threshold. Scope to be amended and advertised as Q62/2021
❖ Q62/2021 Provision of occupational health and safety services (client agent), New Fire Station, Robertson	<i>Advertised on 21 January 2022</i>	Closed 04 February 2022 Report submitted to BEC on 21 February 2022. Await BAC outcome	
❖ Tender - Refurbishment of cloakrooms, van zyl street sports grounds	<i>Detailed specifications submitted to the Community Services Directorate on 15 November 2021.</i>	To date no BSC has taken place and the PMU department awaits further instruction from the Manager Community Facilities.	
❖ T06/2022 Electrification of 172 Formal Houses at Nkqubela, Robertson	<i>Advertised on 25 February 2022</i>	Closing on 04 March 2022	
❖ T59/2021 Supply and installation of gates informal trading areas, Bonnievale and Montagu	<i>Advertised 15 October 2021, closed 05 November 2022</i>	Awarded in January 2022, Contractor indicated that they will be on site in March 2022	
❖ T74/2021 Construction and renovations – Robertson Traffic Offices, Langeberg Municipality	<i>Advertised on 11 February 2022</i>	Tender closes 04 March 2022	
❖ Tender XX_2021 Construction and development of Ashton Silo's cemetery expansion	<i>Await the detailed designs from the professional services department which are expected in 1st week in March. See T39/2021 – Development of Ashton Silo's Cemetery expansion</i>	Construction tender will be called once design and tender document finalised – estimated mid-March 2022	

❖ Tender XX_2021 Construction of fire station, Langeberg Municipality	<i>See T27/2021</i>	Construction tender will be called once design and tender document finalised – estimated mid-August 2022	
❖ Tender XX_2021 Construction of new spectator ablution facilities, Cogmanskloof sports grounds			Tender not to proceed in current book-year. Community Services to indicate way forward.
❖ Tender XX_2022 Resurfacing of Netball Courts, Langeberg Municipality	<i>Detailed specifications and pricing schedule submitted to the Manager Community Facilities on 09 February 2022.</i>	Await BSC outcome	

OPERATIONAL PROJECTS

Project Details	Project Cycle Status and Progress	Mid Term Status – (In-put)	Final Phase Status (Output)
❖ Q43/2021 – Professional services – design and related services: Electrification of Housing project erf 136, Nkqubela	<i>Advertised on 03 September 2021 Closed 17 September 2021 Two documents received which were above the threshold of a quotation. Quotation not awarded as it is above the threshold.</i>	Has been advertised again under T64/2021	Not awarded
❖ Q40/2021 – Service repairs of 7 x LMS Switchgear at Montagu main substation	<i>Quotation not awarded as it is above the threshold</i>	To be undertaken by the Electrical Engineering Department	Not awarded
❖ Q39/2021 – Appointment of a suitably qualified architectural professional with sufficient heritage experience	<i>Advertised on 03 September 2021 Closed 17 September 2021 Report submitted to the BEC on 28 September 2021. BEC report served at BAC on 29 October 2021 Award made and within the 21 day appeals period</i>	Architect appointed and detailed survey undertaken by the professional service provider. Detailed plans and report are expected by early February 2022. Initial reports received final report and specifications expected mid-February 2022 Final report received and submitted to the Director Community Services and Manager Community Facilities for commentary. Report submitted to Heritage Western Cape and they have approved the proposed plan and specifications.	The tender for the construction / repairs to be advertised in March 2022.
❖ T57/21 Supply and Delivery of Transformers, Large Frame Circuit Breakers, Maximum Demand Meters and 3 Phase 4 Wire Meters	<i>Advertised on 02 October 2021. Tender closed 29 October 2021.</i>	Technical evaluation underway. Award made and currently in 21day appeals period No appeals and tender awarded – Stores and Electrical department to place orders when required	Tender awarded – Stores and Electrical department to place orders when required
❖ T61/2021 Supply And Delivery of Combined	<i>Advertised 15 October 2021. Tender closed on 12 November 2021.</i>	Report submitted to the BEC for consideration.	Tender awarded – Stores and Electrical department

Nec/Ner/Aux Transformer, Langeberg Municipality	<i>Await compliant documents from the BEC</i>	Award made and currently in 21-day appeals period No appeals and tender awarded – Stores and Electrical department to place orders when required	to place orders when required
❖ Q10/2022 Painting of roof structure, Robertson Town Hall	<i>Detailed specifications submitted to BSC on 14 February 2022</i>	Await BSC outcome	
❖ Q50/2021 Paintworks at the Robertson Centralised Inventory Stores			Works completed February 2022. Pictures attached.
❖ Tender XX_2022 Painting of Sunnyside, Zolani (Cape Access), Happy Valley and Bonnievale Libraries, Langeberg Municipality	<i>Await BSC compilation by MM office.</i>		

Recommendation / Aanbeveling

That the report be noted. / Voorgelê vir kennisname.

Air Conditioners




Thatch Roof – McGregor



Netball Courts



Montagu Parks – Aluminium Doors

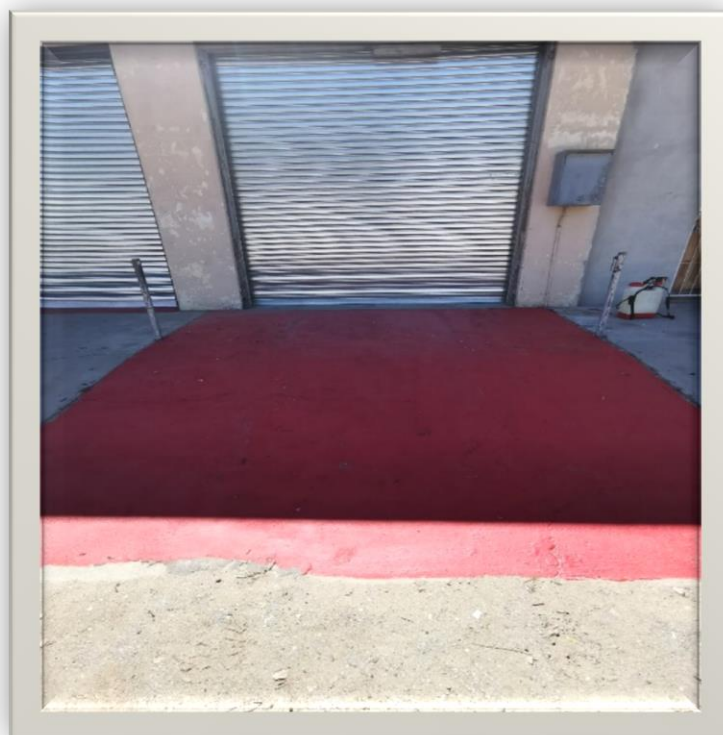

Housing Project Erf 136, Nkqubela (68 units)



Painting of Robertson Stores

